

Status of Bond Projects
8/12/14 Governing Board Meeting


President Zibrat, Board Members, Mr. Nelson,
Current Project Update:

I. INSTRUCTIONAL SPACE / PORTABLE REPLACEMENT

A. Cross Middle School Addition / Remodel:
Construction is 98% complete.
500 wing classroom renovations are complete and in use.



New Cross Choices Room

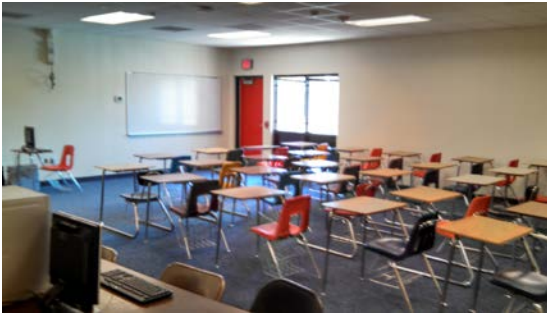

Three New Typical Classrooms & Two New Distance Learning Classrooms



Renovated Cross Categorical Classroom



New ADA Compliant Restroom in
Cross Categorical Classroom

New weight room is complete and in use.



New Weight Room

Site work, including a new bus loop and storm water evacuation improvements are complete.



Cross New Bus Loop



Cross Storm Water Evacuation Improvements

The Administration Building improvements which include a renovation of the reception area, a staff restroom addition, and a health addition and renovation are complete and in use.



Renovated Health Office Reception



Health Office Addition - Triage



Health Office Addition-Triage Work Area




West Vestibule Addition - Staff Restrooms

Campus wide restroom renovations and additions are complete and in use.
Covered walkway repairs in the 100 through 400 wings are complete.



Renovated Covered Walkways

Sound attenuation in the MPR is complete.

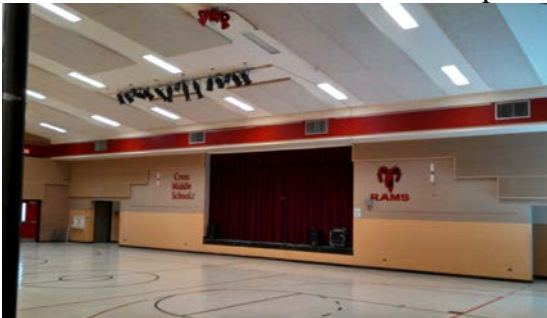

New mass notification system (fire alarm system) is complete and in use.
New security fence is installed and final painting is in process during “off hours.”



New Security Fence

Campus wide re-cabling is complete.



New MDF (main distribution frame)

Punch list corrections and above ceiling demolition of abandoned systems are in process during “off hours.”

The Cross project is on schedule and on budget.

B. Harelson Elementary School Addition / Remodel:
Construction is 98% complete.
The new classroom building is complete and in use.



New Harelson Classroom Building



Two New Typical Classrooms



New Computer Lab and Video
Presentation Room

The new music room added to the south side of the Fun House is complete and in use.



New Harelson Music Room

Renovation of the fourth grade pod building is complete and in use.



Four Renovated Classrooms (4th grade pod)

Restroom additions and renovations are complete and in use.



New Restroom in New Harelson Classroom Building

Storm water evacuation improvements are complete.

New security fence is installed and final painting is in process during “off hours.”



Storm Water Evacuation Improvements



New Campus Security Fence

Campus wide re-cabling is complete.



New IDF (intermediate distribution frame)

Punch list corrections and above ceiling demolition of abandoned systems are in process during “off hours.”

The Harelson Project is on schedule and on budget.

C. Wetmore Professional Development Building:

Tonight’s consent agenda contains a GMP (guaranteed maximum price) for this project for Governing Board review and approval. If approved, work on this project will begin in late August.

D. Donaldson Elementary School Addition / Remodel:

Schematic Design is complete and Design Documents are being developed.

E. Mesa Verde Elementary School Addition / Remodel:

Schematic Design is complete and Design Documents are being developed.

II. HEALTH, SAFETY, & SECURITY

A. Wilson K-8 Health Office Renovation & Security Fencing Installation:

Construction is 96% complete.

The renovated health office is 98% complete and in use. Punch list and above ceiling corrections are in process during “off hours.”



Wilson Health Office Reception



Wilson Health Office Work Area



Wilson Health Office Triage Bay

The new security fence is complete.



New Security Fence and Pedestrian Gates

The Wilson project is on budget and on schedule.

III. NEW SCHOOL

A. New Elementary School:

Tonight's consent agenda contains a recommendation for an architect for this project for Governing Board review and approval. If approved, programming and design for this project will start in late August.
