

Status of Bond Projects
8/8/17 Governing Board Meeting

President Grant, Board Members, Mr. Jaeger
Current Project Update:

I. INNOVATION ACADEMY

A. New Elementary School:
Punch list item work is ongoing site-wide



Center Campus



Solar Array and Canopy's

**Innovation Academy Is Complete
On Time and On Budget**

II. Keeling Elementary

A. Design & Renovation

Roof punch work is scheduled for 7/31

Electrostatic wrought iron painting was 50% complete the week of 7/24

Exterior painting and sealing of buildings including door & window frames is scheduled for completion 8/4

IT cabling upgrades are ongoing



Keeling Blue



Roof at Keeling Annex



Keeling Administration Roof

III. Amphitheater High

A. Renovation and Renewal

Tennis court concrete slabs and enclosures are complete

Fencing around tennis courts began 7/24 and substantial completion is expected by August 18th

200, 300 & 400 classrooms are complete with punch work ongoing in hallways including cove base and floor stencils

HVAC punch work is ongoing

Football Stadium: visitor bleacher dirt work and compaction are complete, bleachers arrived the morning of 7/24, installation scheduled for 3 weeks

Building 700 renovations: floor grinding and polishing is ongoing, ceiling grid and lighting is ongoing, millwork installation was scheduled for the week of 7/24, wrought iron is ongoing

Chiller P.O. (SFB) has been issued, demo was scheduled to begin 7/24

Estimated completion is 8/7/17




Tennis Court Post-tension Work



Building 700 Renovation



Grinding Classroom Concrete Floor

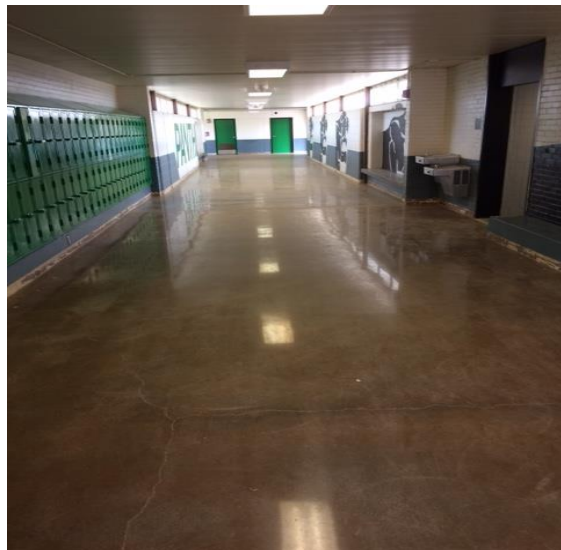

Polished Concrete Floor

IV. Canyon Del Oro

A. Renovation and Renewal

D building – HVAC is complete and inspection was scheduled for 7/24,
installation of ceiling grid and tiles is complete, locker painting is complete
LED lighting in halls and classrooms is 98% complete as of 7/24

Punch walk was scheduled for 7/26

E building – Complete

F building – Complete

R building – Complete

G building – Complete

South gym – Complete

North gym – Lighting is ongoing



D Building HVAC Work



South Gym Padding and Painting

V. Ironwood Ridge

A. Renovation and Renewal

Lighting upgrade is ongoing

Buildings A, B, C & D are complete (sensors are being programmed)

Building E is ongoing

Buildings F and G to follow

This is night work from 4.00pm until 2:00am

Gym roof and Gym block walls are with the SFB

VI. Sand Volleyball

A. Design

Proposed site locations have been delivered to the Athletic Director

Design will be complete 4 weeks after locations are confirmed

Pre-design walks were completed with Breckenridge Architecture at all three High Schools
